



# South San Francisco Caltrain Station Improvement Project

Citizens Advisory Committee

September 15, 2021

Agenda Item 9

# Outline

---

- Scope
- Schedule
- Status
- Next

---

# Scope

# Scope: Project Purpose

---


- Improve station and system operations
- Improve safety
- ADA compliance
- Provide access to City Downtown and improve east-west connection
- Prepare station for electrification infrastructure

# Scope: Key Elements



- New center platform
- Track and signal work
- Pedestrian underpass
- 2 new entries/exits
- Downtown plaza
- ADA access
- Shuttle pick-up/drop-off

# Scope: Key Elements

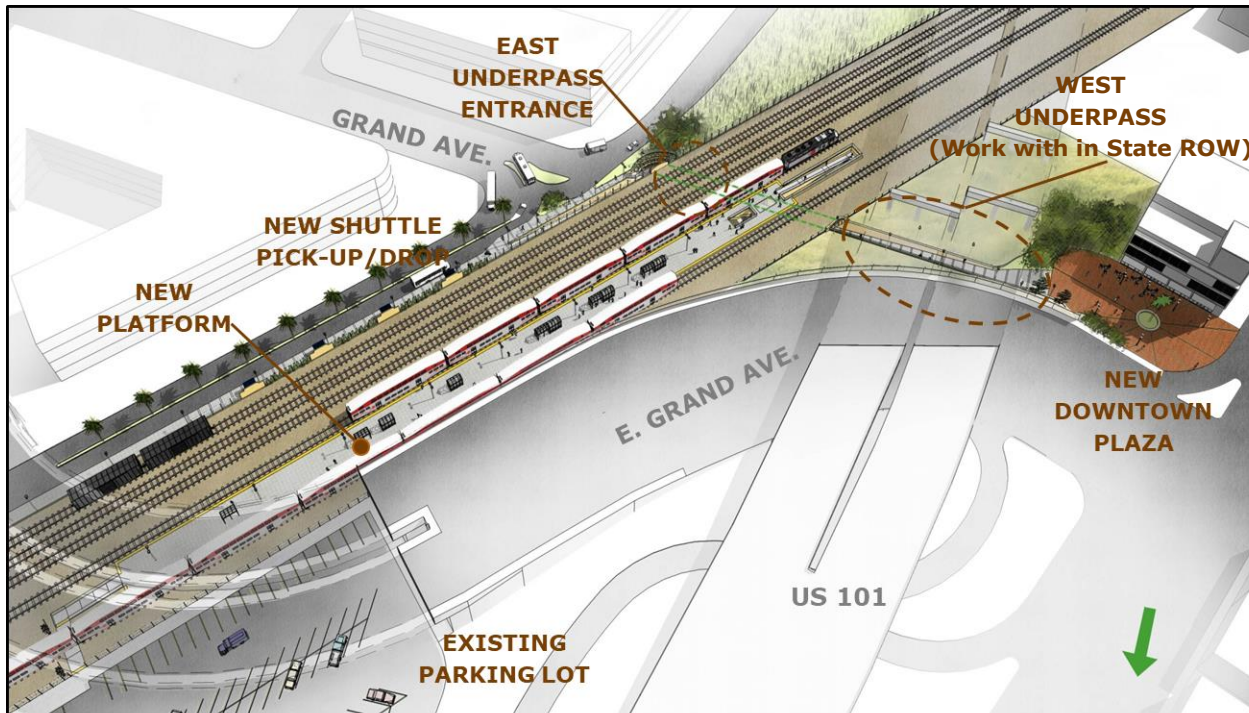

- Shuttle pick-up/drop-off (Eastside Entry)
- 3 Ramps & 2 Stairs
- Pedestrian underpass
- New center platform
- Downtown (West) plaza
- Track and signal work

---

# Schedule

# Schedule: Project Milestones

---

Activity	Date
Bid & Award	April 2017 – August 2017
Begin Construction	November 2017
Partial Suspension	April 2018 – September 2019
Construction Resume	Current – November 2021



---

# Status

# Status: Construction Update

---

Completed Work	<ul style="list-style-type: none"><li>• Shuttle Pick-Up/Drop-Off (Eastside Entry)</li><li>• Pedestrian Underpass</li><li>• 3 ADA Ramps &amp; 2 Stairs</li><li>• New Center Board Platform</li><li>• West Plaza</li><li>• Track &amp; Signal Work (JPB Main Lines &amp; UPRR Yard Tracks)</li></ul>
Work in Progress	<ul style="list-style-type: none"><li>• Testing &amp; Commissioning of Passenger Information Systems</li><li>• Demolish Temp Station Platforms</li><li>• Refinish Parking Lot</li><li>• Mini High Installation</li><li>• Landscaping</li></ul>

# Status – Shuttle Pick-Up (East)

---



Construction of Shuttle Pick-Up

# Status – Ramp 1 & Stair 1

---



# Status – Ped Underpass



---



Rendering of Pedestrian Underpass

# Status – Ped Underpass

---

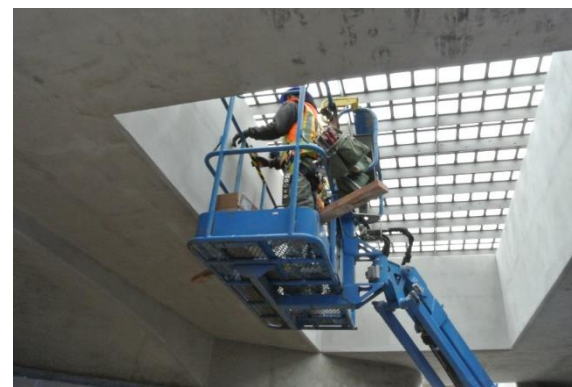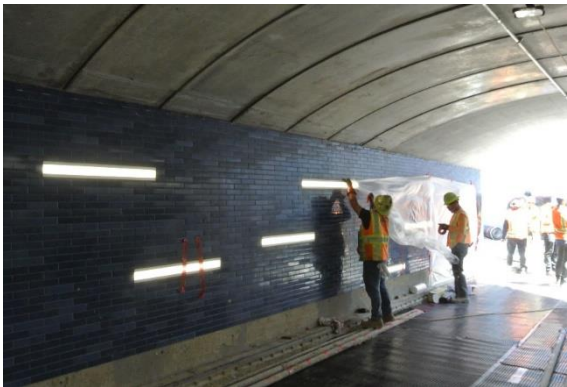

Pedestrian Underpass During Construction

# Status – Ramp 2 & Stair 2

---



# Status – New Platform

---




Rendering of Center Platform



# Status – New Platform

---

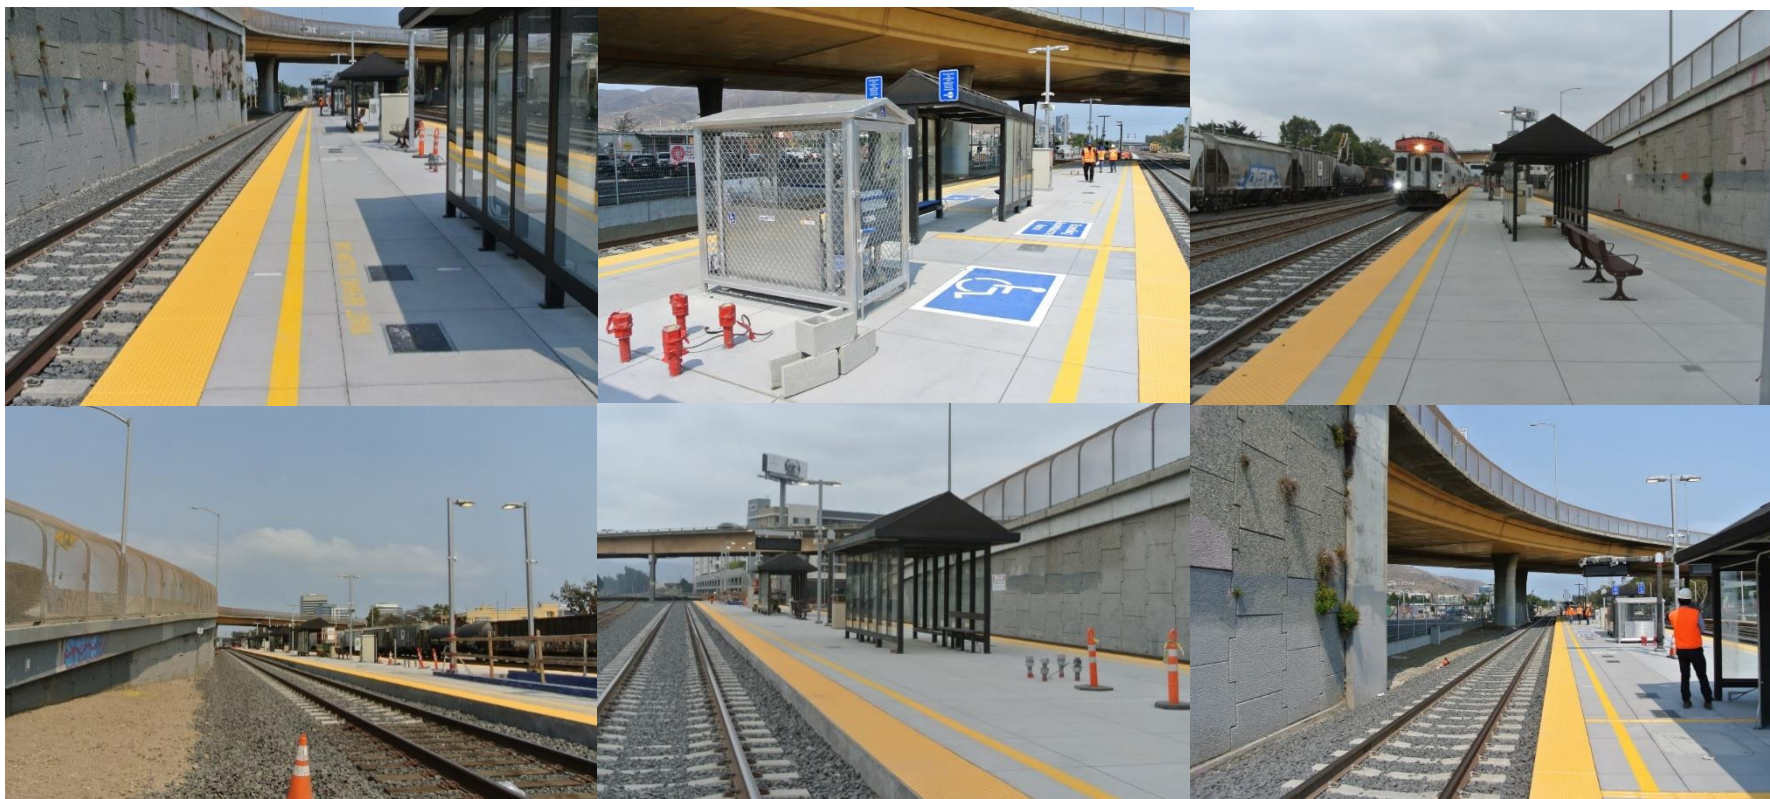

Center Platform During Construction

# Status – Ramp 3

---



# Status – West Plaza

---



Station West Access – West Plaza

# Status – West Plaza

---



Construction of West Station Access

# Status – Track & Yard Work

---



Mainline Tracks & Yard Tracks Work

---

Next

# Next

---

- Soft SSF Station Opening: End of September 2021
  - Demo Current Temp Station Platform
  - Landscaping
  - Refinish Station Parking Lot
- Open SSF Station: November 2021
- Close Contract: December 2021
- Project Close Out

---

Questions?
